

Four next checks after your results

Controls and V064-V063 confirmed. V053-V071 rejected. V090 to V095/V100/V103/V107: all OL.


Battery and programmer disconnected. Report actual resistance, OL or changing. Compare near-zero readings with your probe/contact baseline and reverse probes to check. A beep alone is not proof of a direct connection.

Test	Fixed probe	Moving probe	What this tests	Reading / reversed if low
B3	V064	V070	Regulated VDD to R18 receiver feed	_____
C5	V095	V100	C43/C44 junction to C16/C29 junction	_____
C6	V095	V103	C43/C44 junction to C13/C14 junction	_____
C7	V095	V107	C43/C44 junction to C10/C11 junction	_____

B3 Is the receiver feed also on regulated VDD?



C5-C7 Do the other four junctions share a node?

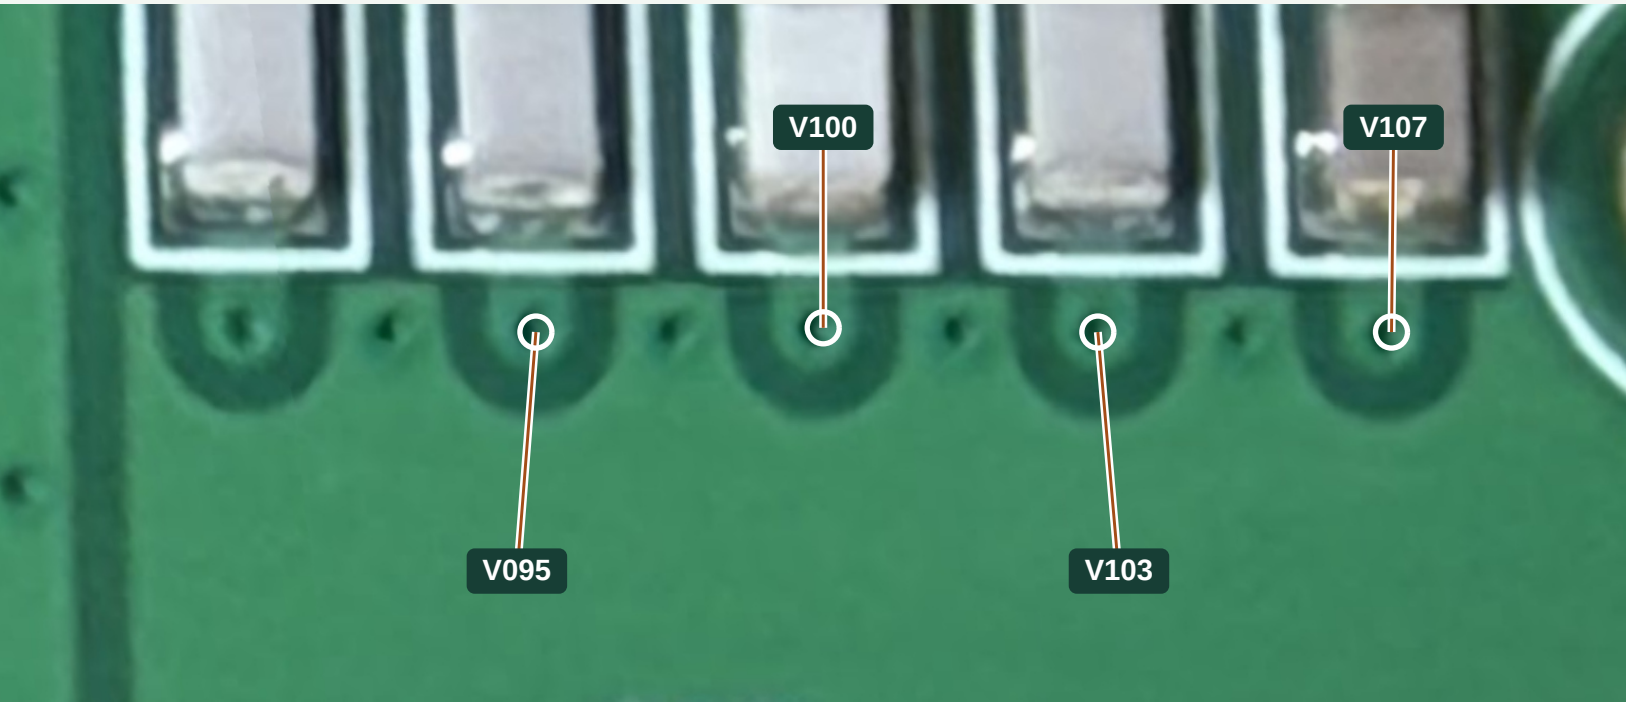

Keep one probe on V095 for all three new C readings. If all are OL, stop broad pairwise testing; we will trace toward antenna/component endpoints instead.

Photographs: rear mosaic already mirrored to match the front. Circles mark vias; leaders are annotations, not traces. Use the paired photo locator for zoomed views. Near-zero can also include an inductor or zero-ohm link.

Next: choose antenna/group tests and remaining RC2/RB0 candidates from these results. Q1 VDD rail choice is still pending.
